BRHAT BANGALORE MAHANAGARA PALIKE

INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads abd Drains From Center Excise Layout to Rail way level crossing (telecom Layout Railway crossing) in Ward No.05 Byatarayanapura Sub Division	
2	Estimate Cost	25.00 Lakhs	
3	Administrative Approved No and Date	577/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	71/13-14, Date. 23.12.2013	
5	Job Code No. and P Code No.	005-14-000044	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applecable	
8	Tender Approved Details	Not Applecable	
9	Work Order No and Date	376/13-14, Date. 21.02.2014	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	21.02.2014	
12	Actiual Date of Completion	31.07.2014	
13	Delay if any	Nil	

14	Reason for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	12.01.2016	
19	BR No. and Date	258/31.07.2014	
20	MB No. and Page No.	Mb No.2504 Page No. 250317-330	
21	Test Result	Quality Test Report submitted by Civil Tech Consultents and Engineers is verified and Enclosed	
22	Section officer	Sri P A Chandrakanthraju A.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	

AE-05

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

12/1/16

Name of work:- Improvements to Roads & Drain from Central Exchange layout to Railway level crossing (Telecom) Railway level crossing in Ward No-05 Byt Sub division

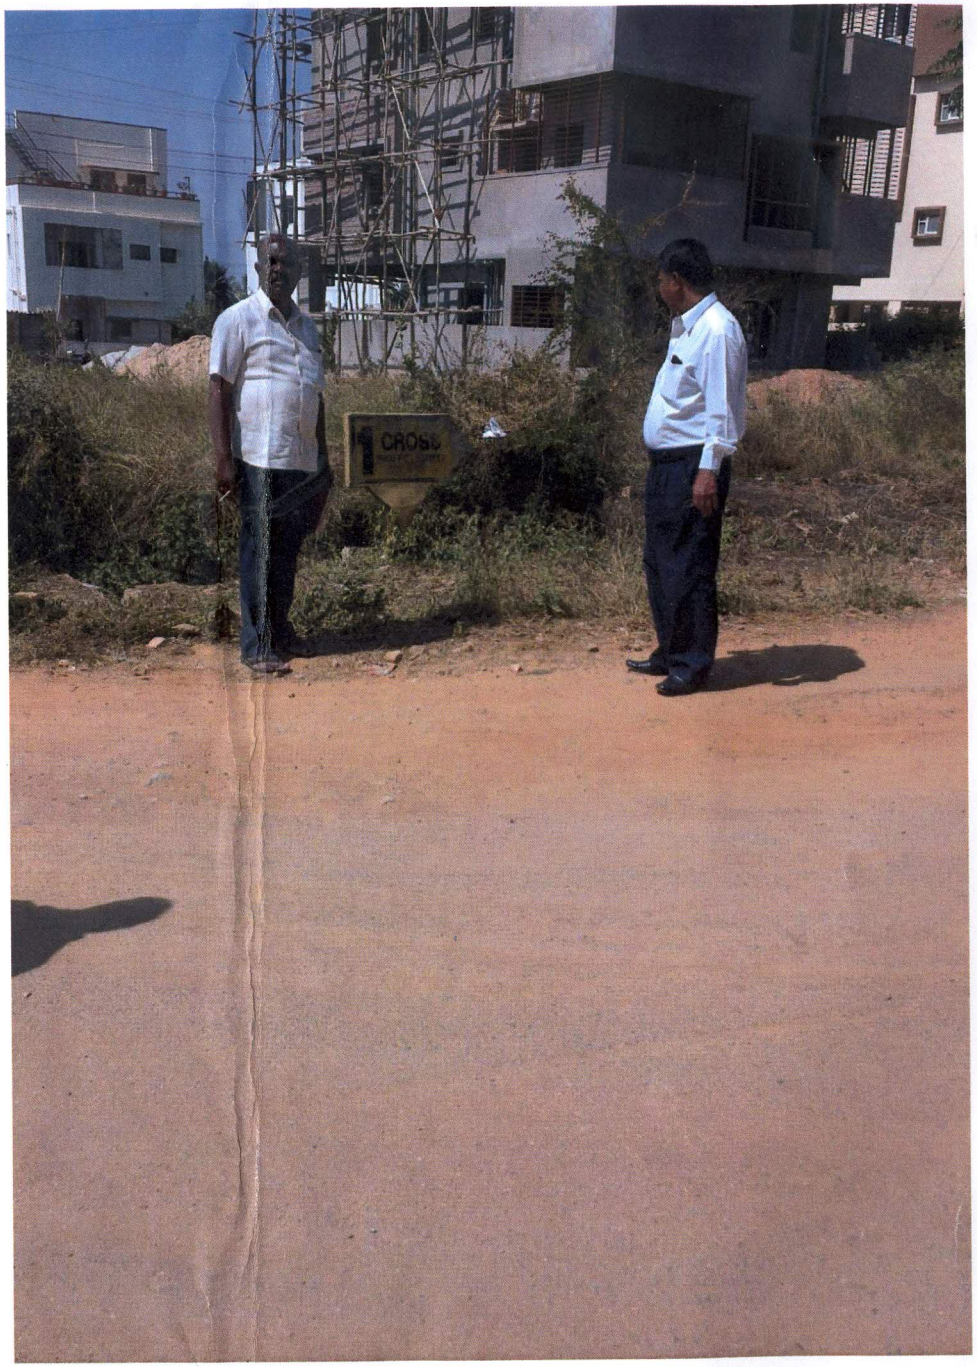

AE-05

ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಎ.ಆರ್.ಡಿ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
